STATE OF CONNECTICUT
DEPARTMENT OF TRANSPORTATION
CHART FOR DETERMINING NUMBER OF CONTRACT DAYS

FOR INFORMATION ONLY
DATE: 10/27/2015

CALENDAR WEEKS
WINTER SHUTDOWN (DEC. 1 to Mar. 31

PREPARED BY (DESIGN UNIT NAME): HIGHWAY DESIGN **DATE:** 10/27/2015

REVIEWED BY (DISTRICT CONSTRUCTION): **DATE:**

FEDERAL AID PROJECT NO. **NA** TOWN **Wethersfield and Glastonbury** PROJ. NO. **159-192**

Pavement Preservation

Construction Season 2016 2017 2018

WORK BEGINNING DATE
(STARTING MONDAYS)

OPERATION	*QUANTITY*
DCD	1/13/2016
DATE OF ADV (Wed)	2/10/2016
DATE OF LETTING (Wed)	3/9/2016
DATE OF AWARD (Fri)	5/6/2016
START OF CONSTRUCTION	6/20/2016
PERMIT RESTRICTIONS	N/A to N/A
UTILITY WORK	0
MOBILIZATION	1
SIDEWALK RAMPS	1
DRAINAGE STRUCTURES	6
MILLING	8
PAVING	9
HIGH FRICTION PAVEMENT TREATMENT	1
	0
BRIDGE JOINTS	6
PAVEMENT MARKINGS	12
ILLUMINATION (Work can be preformed in conjunction with pavement operation)	
SHOP DRAWINGS REVIEW & PROCUREMENT OF MATERIALS	8
TRENCHING, CABLE AND FOUNDATION INSTALL FROM NAUBUC TO RTE	12
INSTALL LIGHT STANDARDS FROM PUTNAM BRIDGE TO NUABUC AVE	4
LIGHT POLE AND LUMINAIRE INSTALL NAUBUC TO RTE 2	7
UNDERBRIDGE LIGHT INSTALL AT NAUBUC AND MAIN ST	3
REMOVAL OF EXISTING POLES AND CLEAN-UP	6
SEMI-FINAL INSPECTIONAND PUNCH LIST RESOLUTION	4
	0

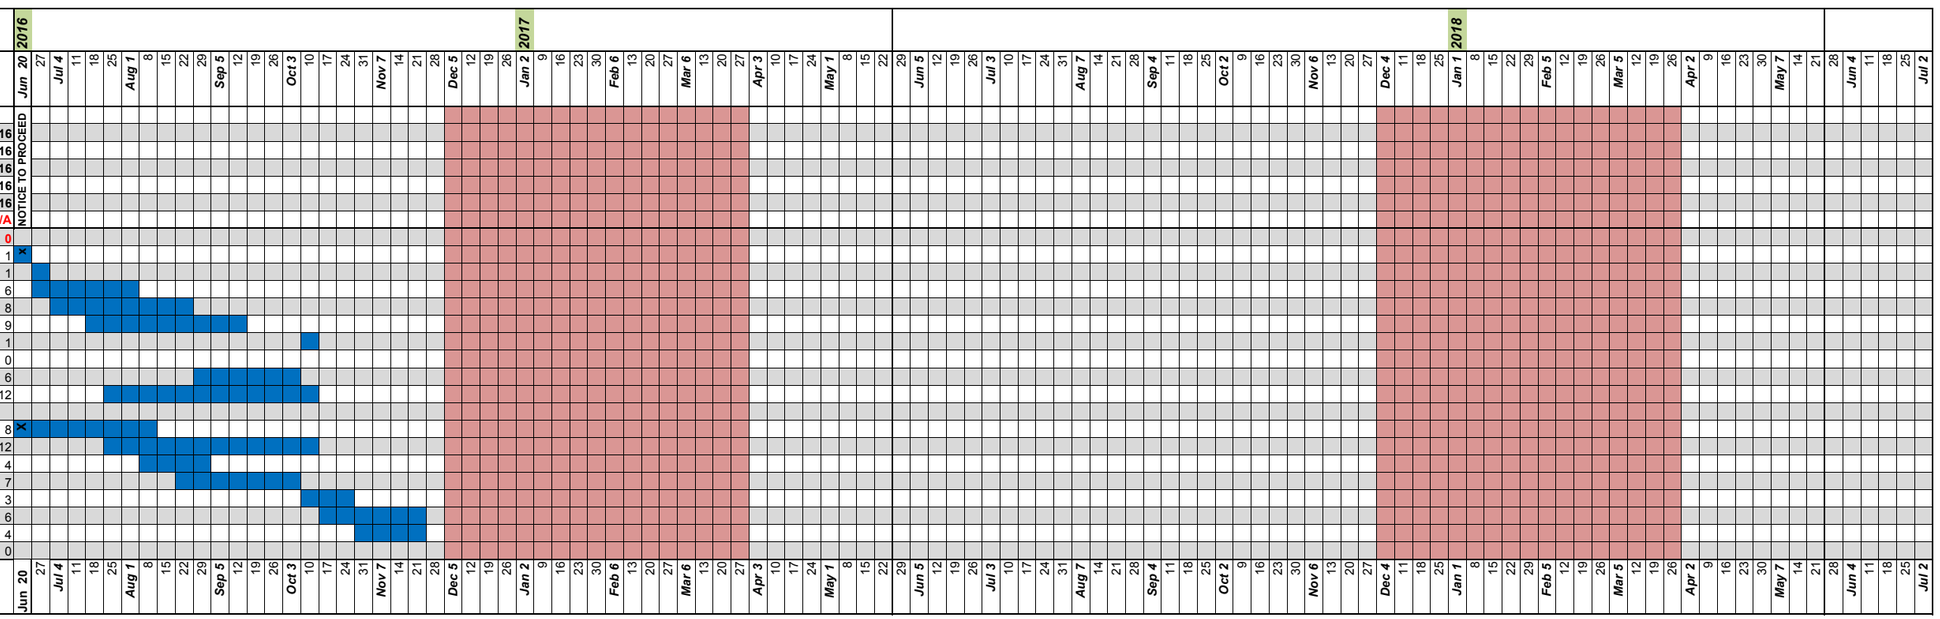

WEEK OF (STARTING MONDAYS)

Printed on: 12/4/2015 15:55

CALENDAR DAYS ALLOWED = 161
